




ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	2017		Qtr 3, 2017			Qtr 4, 2017			Qtr 1, 2018			Qtr 2, 2018			Qtr 3, 2018	
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Northcote Safe Cycle Route Stage 1	255 days	Mon 10/07/17	Tue 24/07/18	Mon 29/05/17	Tue 1/05/18																
2	Pre Construction	255 days	Mon 10/07/17	Tue 24/07/18	Mon 29/05/17	Tue 1/05/18																
3	AT Approval to Begin Works	0 days	Mon 10/07/17	Mon 10/07/17	Mon 12/06/17	Fri 30/06/17																
4	Construction Begins	0 days	Wed 12/07/17	Wed 12/07/17	Fri 30/06/17	Fri 30/06/17																
5	Project Complete	0 days	Mon 25/06/18	Mon 25/06/18	Tue 1/05/18	Tue 1/05/18																
6	Inclement Weather Allowance	37 days	Fri 1/06/18	Tue 24/07/18	NA	NA																
7	Construction	232 days	Wed 12/07/17	Mon 25/06/18	Wed 12/07/17	Tue 1/05/18																
8	Stage 1 - Northcote Rd	226 days	Wed 12/07/17	Mon 18/06/18	Tue 18/07/17	Mon 11/12/17																
9	Stage 1A - CH10-CH260	226 days	Wed 12/07/17	Mon 18/06/18	Tue 18/07/17	Wed 9/08/17																
10	Southside Footpath CH260 -CH10	9 days	Wed 12/07/17	Tue 25/07/17	NA	NA																
19	Northside Footpath CH10 - CH260	10 days	Wed 26/07/17	Tue 8/08/17	NA	NA																
26	Taharoto Intersection	5 days	Thu 31/05/18	Thu 7/06/18	Fri 22/09/17	Thu 2/11/17																
27	Excavate / Demo existing	1 day	Thu 31/05/18	Thu 31/05/18	NA	NA																
28	Install Kerbs	1 day	Fri 1/06/18	Fri 1/06/18	NA	NA																
29	Install Tactile / Directional Pavers	1 day	Tue 5/06/18	Tue 5/06/18	NA	NA																
30	Install New Signals	1 day	Fri 1/06/18	Fri 1/06/18	NA	NA																
31	Install Furniture Items	1 day	Fri 1/06/18	Fri 1/06/18	Fri 22/09/17	Fri 29/09/17																
32	Concrete or AC	2 days	Wed 6/06/18	Thu 7/06/18	Mon 2/10/17	Wed 4/10/17																
33	Stage 1A - Snag Items	7 days	Fri 8/06/18	Mon 18/06/18	NA	NA																
34	Streetlights Smales Farm	5 days	Fri 8/06/18	Thu 14/06/18	NA	NA																
35	Snags	2 days	Fri 15/06/18	Mon 18/06/18	NA	NA																
36	Stage 1B - CH500-CH1000	170 days	Wed 9/08/17	Tue 24/04/18	Wed 9/08/17	Tue 19/09/17																
37	Golf Club Footpath CH500 - CH720	11 days	Wed 9/08/17	Wed 23/08/17	NA	NA																
46	Netball Footpath CH500 - CH820	11 days	Wed 23/08/17	Thu 7/09/17	NA	NA																
55	Rugby Club Footpath CH820 - CH1000	15 days	Tue 12/09/17	Mon 2/10/17	NA	NA																
62	Backyard Garage Footpath CH740 - CH1000	9 days	Mon 13/11/17	Fri 24/11/17	NA	NA																
71	Stage 1B - Snag Items	30 days	Mon 12/03/18	Tue 24/04/18	NA	NA																
72	Tidy Up Snags	5 days	Wed 18/04/18	Tue 24/04/18	NA	NA																
73	Fencing	10 days	Mon 12/03/18	Fri 23/03/18	NA	NA																
74	Landscaping Outside Rugby Club	2 days	Mon 16/04/18	Tue 17/04/18	NA	NA																
75	Stage 1C - CH1040-CH1380	26 days	Mon 2/10/17	Wed 8/11/17	Tue 19/09/17	Tue 17/10/17																
76	Southside Footpath CH1080-1340	13 days	Mon 2/10/17	Thu 19/10/17	NA	NA																
85	Northside Footpath CH1080 - CH1340	13 days	Fri 20/10/17	Wed 8/11/17	NA	NA																
93	Stage 1D - Lake / Ocean Roundabout	99 days	Wed 8/11/17	Fri 13/04/18	Tue 19/09/17	Mon 9/10/17																
94	Set Up TMP Stage 1	0 days	Wed 8/11/17	Wed 8/11/17	NA	NA																
95	Remove Roundabout	3 days	Wed 8/11/17	Fri 10/11/17	NA	NA																
96	Set Up TMP Stage 2	0 days	Fri 10/11/17	Fri 10/11/17	NA	NA																
97	Remove Islands	3 days	Fri 10/11/17	Tue 14/11/17	NA	NA																
98	Construct new exterior elements (Footpaths, kerbs, etc)	15 days	Wed 17/01/18	Thu 8/02/18	NA	NA																
99	Construct New Roundabout	10 days	Tue 27/03/18	Wed 11/04/18	NA	NA																
100	Construct Speed Tables	32 days	Fri 9/02/18	Mon 26/03/18	NA	NA																

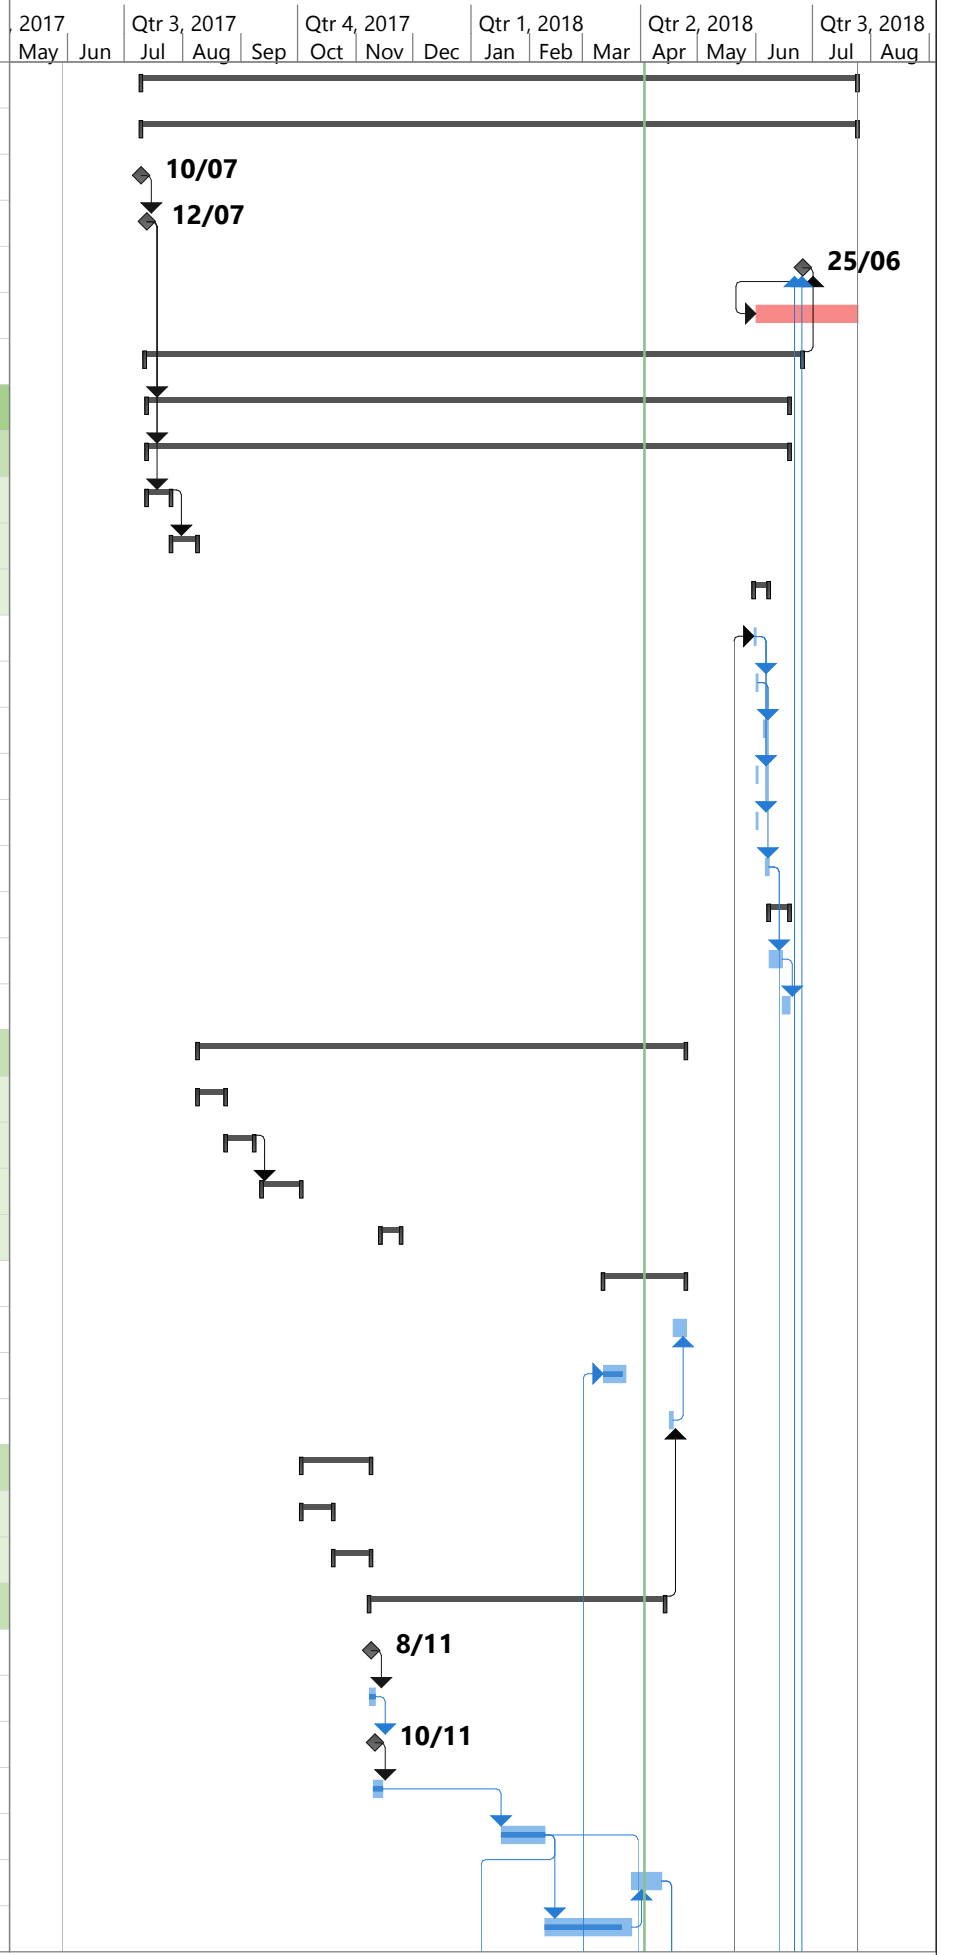


ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	2017		Qtr 3, 2017			Qtr 4, 2017			Qtr 1, 2018			Qtr 2, 2018			Qtr 3, 2018	
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
101	Asphalt	2 days	Thu 12/04/18	Fri 13/04/18	NA	NA																
102	Stage 1E - Northcote/Akoranga Intersection	77 days	Wed 17/01/18	Thu 10/05/18	Fri 22/09/17	Thu 2/11/17																
103	Ducting	8 days	Wed 17/01/18	Fri 26/01/18	NA	NA																
104	Excavate / Demo existing	3 days	Tue 30/01/18	Thu 1/02/18	NA	NA																
105	Install Tactile / Directional Pavers	5 days	Thu 12/04/18	Wed 18/04/18	NA	NA																
106	Install New Signals	4 days	Fri 2/02/18	Thu 8/02/18	NA	NA																
107	Install Furniture Items	2 days	Thu 19/04/18	Fri 20/04/18	Fri 22/09/17	Fri 29/09/17																
108	Concrete islands / footpath	13 days	Mon 23/04/18	Thu 10/05/18	Mon 2/10/17	Wed 4/10/17																
109	Stage 1 - Line-marking & Signage	6 days	Fri 8/06/18	Fri 15/06/18	Wed 18/10/17	Tue 31/10/17																
110	Painting	3 days	Fri 8/06/18	Tue 12/06/18	Wed 18/10/17	Fri 20/10/17																
111	Greening	4 days	Mon 11/06/18	Thu 14/06/18	Thu 19/10/17	Thu 26/10/17																
112	Long Life	4 days	Tue 12/06/18	Fri 15/06/18	Tue 24/10/17	Tue 31/10/17																
113	Stage 2 - Lake Rd	78 days	Mon 12/02/18	Tue 5/06/18	Tue 12/12/17	Mon 30/04/18																
114	Stage 2A - Eastside Footpath CH1460 - CH1860	35.98 days	Mon 12/02/18	Wed 4/04/18	NA	NA																
115	Set Up TMP	0 days	Mon 12/02/18	Mon 12/02/18	NA	NA																
116	Excavate To Waste	3 days	Mon 12/02/18	Wed 14/02/18	NA	NA																
117	Utilities Relocations (Inc New Lights)	2 days	Wed 14/02/18	Tue 27/03/18	NA	NA																
118	Subsoil Installation	3 days	Wed 14/02/18	Wed 28/03/18	NA	NA																
119	Prep Parking Bays	2 days	Fri 16/02/18	Wed 28/03/18	NA	NA																
120	Kerbing Works	2 days	Tue 20/02/18	Thu 29/03/18	NA	NA																
121	Footpath Bascourse Preparation and Boxing	3 days	Thu 22/02/18	Tue 3/04/18	NA	NA																
122	Pour New Footpath	3 days	Fri 23/02/18	Thu 29/03/18	NA	NA																
123	Remove Boxing and landscape	2 days	Tue 27/02/18	Thu 29/03/18	NA	NA																
124	Install Fence and Furniture Items	2 days	Thu 29/03/18	Wed 4/04/18	NA	NA																
125	Stage 2B - School & Countdown CH1860 - CH2200	42 days	Mon 5/03/18	Fri 4/05/18	NA	NA																
126	Set Up TMP	0 days	Mon 5/03/18	Mon 5/03/18	NA	NA																
127	Excavate To Waste	5 days	Mon 5/03/18	Tue 3/04/18	NA	NA																
128	Utilities Relocations (Inc New Lights)	3 days	Thu 8/03/18	Tue 3/04/18	NA	NA																
129	Subsoil Installation	5 days	Thu 8/03/18	Thu 5/04/18	NA	NA																
130	Prep Parking Bays	5 days	Fri 6/04/18	Thu 12/04/18	NA	NA																
131	Kerbing Works	4 days	Tue 20/03/18	Fri 13/04/18	NA	NA																
132	Footpath Bascourse Preparation and Boxing	6 days	Mon 26/03/18	Fri 20/04/18	NA	NA																
133	Pour New Footpath	4 days	Thu 29/03/18	Fri 20/04/18	NA	NA																
134	Remove Boxing and landscape	3 days	Thu 19/04/18	Mon 23/04/18	NA	NA																
135	Construct speed Tables	6 days	Tue 24/04/18	Wed 2/05/18	NA	NA																
136	Install Fence and Furniture Items	2 days	Thu 3/05/18	Fri 4/05/18	NA	NA																
137	Stage 2C - West Footpath CH2200 - CH1770	16 days	Wed 11/04/18	Thu 3/05/18	NA	NA																
138	Set Up TMP	0 days	Thu 12/04/18	Thu 12/04/18	NA	NA																
139	Excavate To Waste	3 days	Wed 11/04/18	Fri 13/04/18	NA	NA																
140	Utilities Relocations (Inc New Lights)	2 days	Fri 13/04/18	Mon 16/04/18	NA	NA																
141	Subsoil Installation	3 days	Fri 13/04/18	Tue 17/04/18	NA	NA																

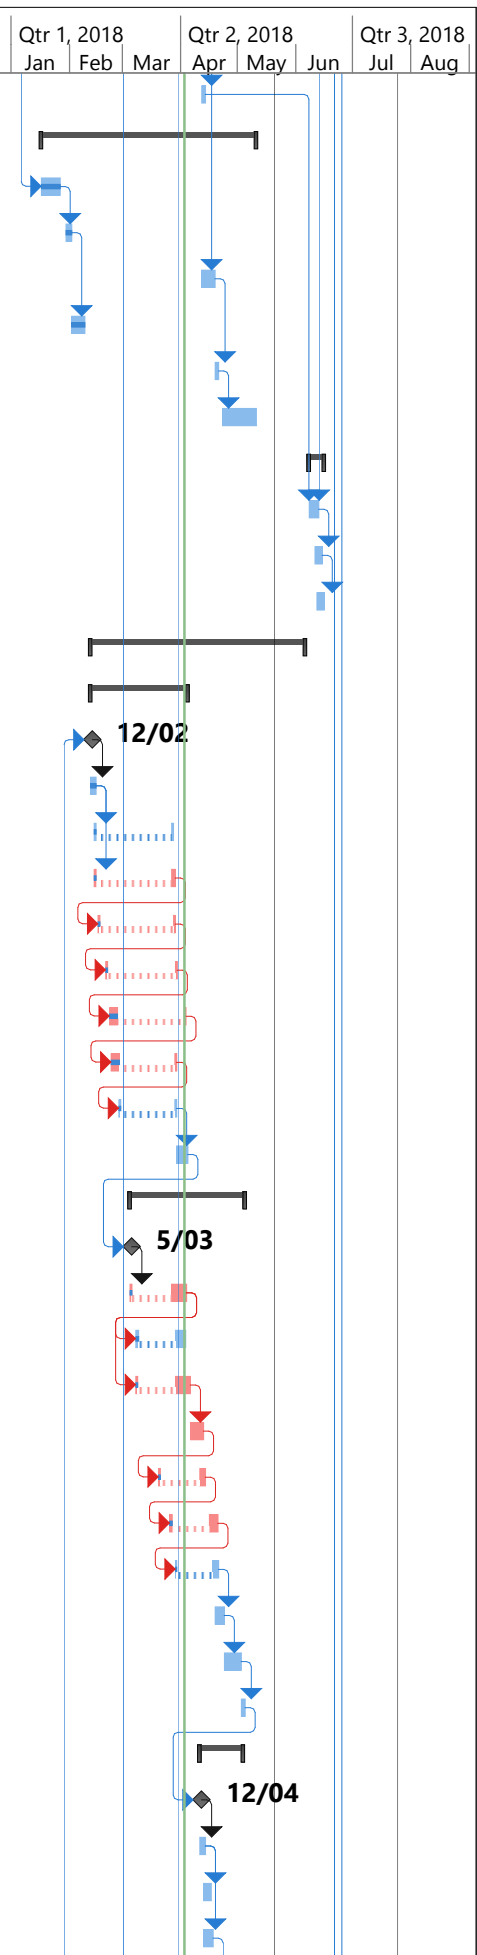


ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	2017		Qtr 3, 2017			Qtr 4, 2017			Qtr 1, 2018			Qtr 2, 2018			Qtr 3, 2018	
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
142	Prep Parking Bays	5 days	Tue 17/04/18	Mon 23/04/18	NA	NA																
143	Kerbing Works	2 days	Tue 24/04/18	Thu 26/04/18	NA	NA																
144	Footpath Bascourse Preparation and Boxing	4 days	Thu 26/04/18	Tue 1/05/18	NA	NA																
145	Pour New Footpath	3 days	Mon 30/04/18	Wed 2/05/18	NA	NA																
146	Remove Boxing and landscape	1 day	Thu 3/05/18	Thu 3/05/18	NA	NA																
147	Stage 2D - West Footpath CH1770 - CH1460	16 days	Fri 4/05/18	Fri 25/05/18	NA	NA																
148	Set Up TMP	0 days	Fri 4/05/18	Fri 4/05/18	NA	NA																
149	Excavate To Waste	3 days	Fri 4/05/18	Tue 8/05/18	NA	NA																
150	Utilities Relocations (Inc New Lights)	2 days	Tue 8/05/18	Wed 9/05/18	NA	NA																
151	Subsoil Installation	3 days	Tue 8/05/18	Thu 10/05/18	NA	NA																
152	Prep Parking Bays	5 days	Thu 10/05/18	Wed 16/05/18	NA	NA																
153	Kerbing Works	2 days	Thu 17/05/18	Fri 18/05/18	NA	NA																
154	Footpath Bascourse Preparation and Boxing	4 days	Fri 18/05/18	Wed 23/05/18	NA	NA																
155	Pour New Footpath	3 days	Tue 22/05/18	Thu 24/05/18	NA	NA																
156	Remove Boxing and landscape	1 day	Fri 25/05/18	Fri 25/05/18	NA	NA																
157	Stage 2E - Lake/Raleigh Intersection	39 days	Tue 3/04/18	Tue 29/05/18	Fri 22/09/17	Thu 2/11/17																
158	Set Up TMP Stage 1	0 days	Tue 3/04/18	Tue 3/04/18	NA	NA																
159	Remove Roundabout	2 days	Wed 4/04/18	Thu 5/04/18	NA	NA																
160	Set Up TMP Stage 2	0 days	Thu 5/04/18	Thu 5/04/18	NA	NA																
161	Remove Islands	4 days	Fri 6/04/18	Wed 11/04/18	NA	NA																
162	Set Up TMP Stage 3	0 days	Wed 11/04/18	Wed 11/04/18	NA	NA																
163	Construct new exterior elements (Footpaths, kerbs, etc)	15 days	Thu 12/04/18	Thu 3/05/18	NA	NA																
164	Set Up TMP Stage 4	0 days	Thu 3/05/18	Thu 3/05/18	Mon 2/10/17	Wed 4/10/17																
165	Construct New Roundabout	8 days	Fri 4/05/18	Tue 15/05/18	NA	NA																
166	Construct New Islands	8 days	Wed 16/05/18	Fri 25/05/18	NA	NA																
167	Asphalt	2 days	Mon 28/05/18	Tue 29/05/18	NA	NA																
168	Stage 2 - Line-marking & Signage	6 days	Mon 28/05/18	Tue 5/06/18	Wed 21/03/18	Tue 3/04/18																
169	Painting	2 days	Mon 28/05/18	Tue 29/05/18	Wed 21/03/18	Fri 23/03/18																
170	Greening	2 days	Wed 30/05/18	Thu 31/05/18	Thu 22/03/18	Thu 29/03/18																
171	Long Life	3 days	Thu 31/05/18	Tue 5/06/18	Tue 27/03/18	Tue 3/04/18																
172	Stage 3 - Lake Rd	120 days	Mon 18/12/17	Mon 25/06/18	Fri 22/12/17	Tue 1/05/18																
173	Stage 3A - East Footpath (Ch2400 - CH2680)	65 days	Mon 26/02/18	Thu 31/05/18	NA	NA																
174	Set Up TMP	0 days	Mon 26/02/18	Mon 26/02/18	NA	NA																
175	Potholing for RW	19 days	Tue 27/02/18	Fri 23/03/18	NA	NA																
176	Retaining Wall 2 Construction	8 days	Fri 13/04/18	Tue 24/04/18	NA	NA																
177	Retaining Wall 3 Construction	8 days	Thu 26/04/18	Mon 7/05/18	NA	NA																
178	Excavate To Waste	5 days	Tue 8/05/18	Mon 14/05/18	NA	NA																
179	Utilities Relocations (Inc New Lights)	2 days	Fri 11/05/18	Mon 14/05/18	NA	NA																
180	Subsoil Installation	2 days	Mon 14/05/18	Tue 15/05/18	NA	NA																
181	Footpath Bascourse Preparation and Boxing	6 days	Wed 16/05/18	Wed 23/05/18	NA	NA																
182	Pour New Footpath	4 days	Tue 22/05/18	Fri 25/05/18	NA	NA																

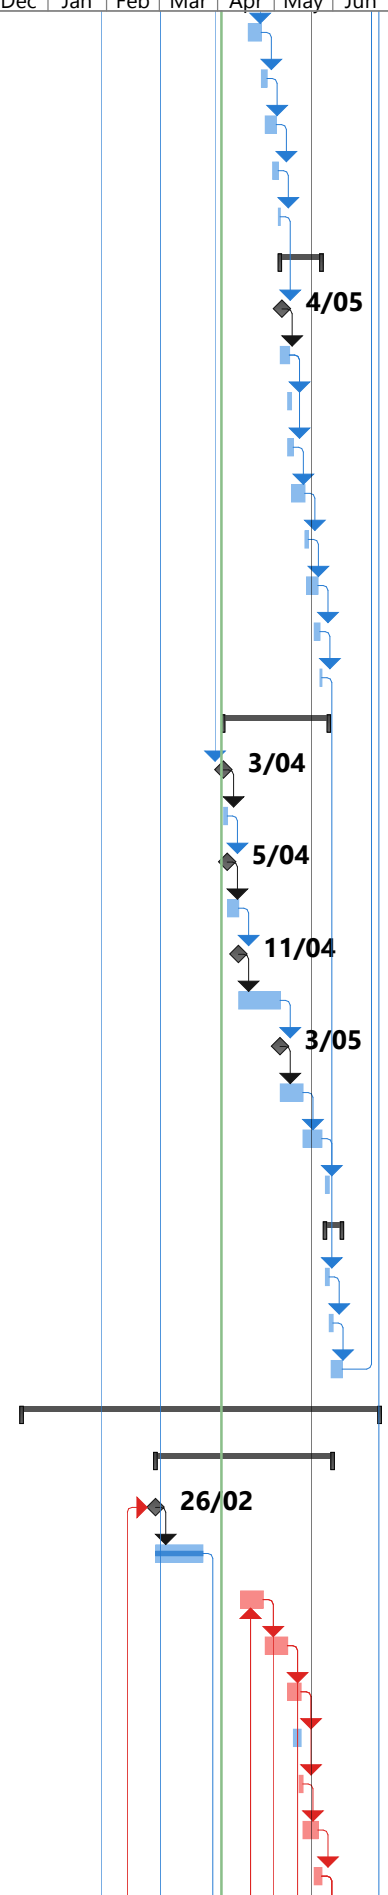

ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	2017		Qtr 3, 2017			Qtr 4, 2017			Qtr 1, 2018			Qtr 2, 2018			Qtr 3, 2018	
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
183	Remove Boxing and landscape	3 days	Fri 25/05/18	Tue 29/05/18	NA	NA																
184	Replace Existing Bus Shelter	2 days	Wed 30/05/18	Thu 31/05/18	NA	NA																
185	Stage 3B - (CH2680 - CH2940)	22 days	Tue 24/04/18	Fri 25/05/18	NA	NA																
186	Set Up TMP	0 days	Tue 24/04/18	Tue 24/04/18	NA	NA																
187	Retaining Wall 5 Construction	8 days	Tue 8/05/18	Thu 17/05/18	NA	NA																
188	Speed Table Construction	5 days	Fri 18/05/18	Thu 24/05/18	NA	NA																
189	Excavate to Waste	6 days	Thu 26/04/18	Thu 3/05/18	NA	NA																
190	Utilities Relocations (Inc New Lights)	2 days	Thu 3/05/18	Fri 4/05/18	NA	NA																
191	Footpath Bascourse Preparation and Boxing	5 days	Wed 2/05/18	Tue 8/05/18	NA	NA																
192	Pour New Footpath	4 days	Fri 18/05/18	Wed 23/05/18	NA	NA																
193	Remove Boxing and landscape	3 days	Tue 22/05/18	Thu 24/05/18	NA	NA																
194	Replace Existing Bus Shelter	1 day	Fri 25/05/18	Fri 25/05/18	NA	NA																
195	Stage 3C - East Footpath (CH2940 - CH3200)	13 days	Fri 25/05/18	Thu 14/06/18	NA	NA																
196	Set Up TMP	0 days	Fri 25/05/18	Fri 25/05/18	NA	NA																
197	Excavate To Waste	6 days	Mon 28/05/18	Tue 5/06/18	NA	NA																
198	Utilities Relocations (Inc New Lights)	2 days	Tue 5/06/18	Wed 6/06/18	NA	NA																
199	Subsoil Installation	2 days	Wed 6/06/18	Thu 7/06/18	NA	NA																
200	Kerbing Works	2 days	Fri 8/06/18	Mon 11/06/18	NA	NA																
201	Footpath Bascourse Preparation and Boxing	6 days	Fri 1/06/18	Mon 11/06/18	NA	NA																
202	Pour New Footpath	4 days	Fri 8/06/18	Wed 13/06/18	NA	NA																
203	Remove Boxing and landscape	3 days	Tue 12/06/18	Thu 14/06/18	NA	NA																
204	Stage 3D - Northcote Primary RW (CH3240 - CH3120)	79 days	Mon 18/12/17	Thu 26/04/18	NA	NA																
205	Set Up TMP	0 days	Mon 18/12/17	Mon 18/12/17	NA	NA																
206	Excavate To Waste	3 days	Mon 18/12/17	Wed 20/12/17	NA	NA																
207	Utilities Relocations (Inc New Lights)	2 days	Thu 21/12/17	Fri 22/12/17	NA	NA																
208	Subsoil Installation	2 days	Thu 21/12/17	Fri 22/12/17	NA	NA																
209	Kerbing Works	2 days	Fri 13/04/18	Mon 16/04/18	NA	NA																
210	Footpath Bascourse Preparation and Boxing	3 days	Tue 17/04/18	Thu 19/04/18	NA	NA																
211	Pour New Footpath	3 days	Fri 20/04/18	Tue 24/04/18	NA	NA																
212	Remove Boxing and landscape	1 day	Thu 26/04/18	Thu 26/04/18	NA	NA																
213	Stage 3E - West Footpath (CH2930 - CH3120)	21 days	Fri 27/04/18	Fri 25/05/18	NA	NA																
214	Set Up TMP	0 days	Fri 27/04/18	Fri 27/04/18	NA	NA																
215	Arborist - Tree Removal Trimming	2 days	Fri 27/04/18	Mon 30/04/18	NA	NA																
216	Excavate To Waste	5 days	Fri 27/04/18	Thu 3/05/18	NA	NA																
217	Utilities Relocations (Inc New Lights)	2 days	Wed 2/05/18	Thu 3/05/18	NA	NA																
218	Subsoil Installation	4 days	Fri 4/05/18	Wed 9/05/18	NA	NA																
219	Kerbing Works	3 days	Thu 10/05/18	Mon 14/05/18	NA	NA																
220	Footpath Bascourse Preparation and Boxing	6 days	Mon 14/05/18	Mon 21/05/18	NA	NA																
221	Pour New Footpath	5 days	Fri 18/05/18	Thu 24/05/18	NA	NA																
222	Remove Boxing and landscape	3 days	Wed 23/05/18	Fri 25/05/18	NA	NA																
223	Replace Furniture Items	1 day	Fri 25/05/18	Fri 25/05/18	NA	NA																

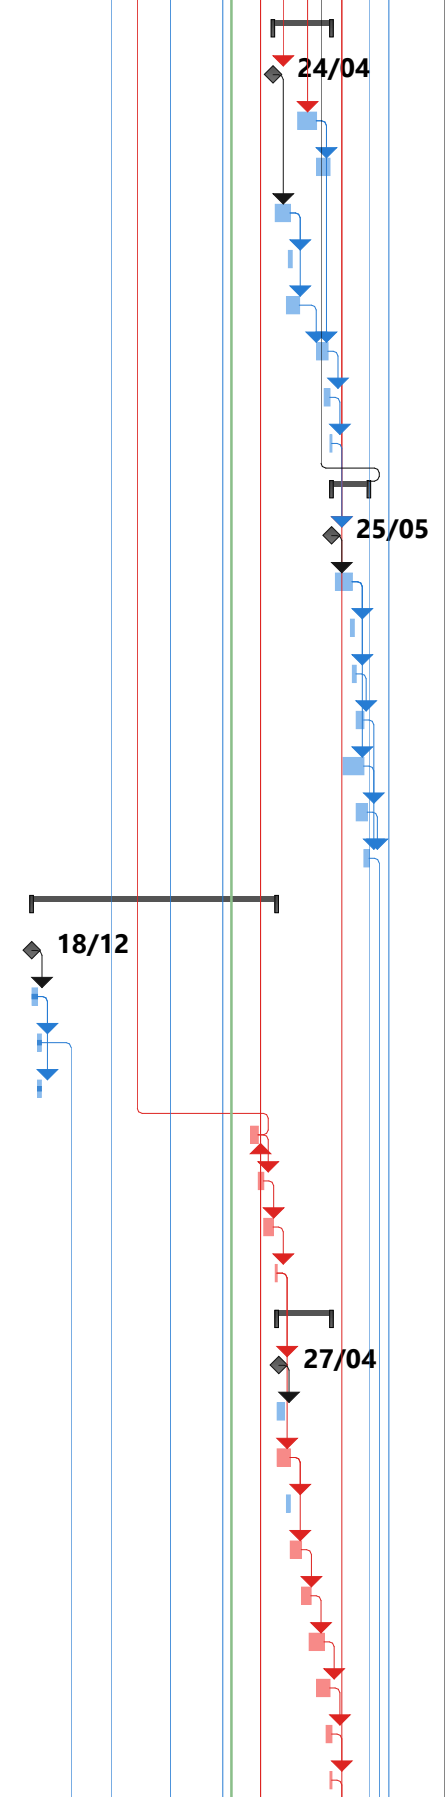

ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	2017		Qtr 3, 2017			Qtr 4, 2017			Qtr 1, 2018			Qtr 2, 2018			Qtr 3, 2018	
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
224	Stage 3F - West Footpath (CH2440 - CH2560)	8 days	Fri 25/05/18	Thu 7/06/18	NA	NA																
225	Set Up TMP	0 days	Fri 25/05/18	Fri 25/05/18	NA	NA																
226	Excavate To Waste	4 days	Mon 28/05/18	Thu 31/05/18	NA	NA																
227	Arborist - Tree Removal Trimming	1 day	Wed 30/05/18	Wed 30/05/18	NA	NA																
228	Subsoil Installation	2 days	Fri 1/06/18	Tue 5/06/18	NA	NA																
229	Kerbing Works	2 days	Thu 31/05/18	Fri 1/06/18	NA	NA																
230	Footpath Bascourse Preparation and Boxing	4 days	Thu 31/05/18	Wed 6/06/18	NA	NA																
231	Pour New Footpath	3 days	Tue 5/06/18	Thu 7/06/18	NA	NA																
232	Remove Boxing and landscape	2 days	Wed 6/06/18	Thu 7/06/18	NA	NA																
233	Stage 3G - Onewa Intersection	12 days	Thu 7/06/18	Mon 25/06/18	NA	NA																
234	Set Up TMP	0 days	Thu 7/06/18	Thu 7/06/18	NA	NA																
235	Excavate / Demo existing	2 days	Fri 8/06/18	Mon 11/06/18	NA	NA																
236	Install Kerbs	2 days	Tue 12/06/18	Wed 13/06/18	NA	NA																
237	Install Tactile / Directional Pavers	3 days	Thu 14/06/18	Mon 18/06/18	NA	NA																
238	Install New Signals	1 day	Tue 19/06/18	Tue 19/06/18	NA	NA																
239	Install Furniture Items	1 day	Wed 20/06/18	Wed 20/06/18	NA	NA																
240	Concrete or AC	3 days	Thu 21/06/18	Mon 25/06/18	NA	NA																
241	Stage 3 - Line-marking & Signage	3 days	Fri 15/06/18	Tue 19/06/18	Wed 21/03/18	Tue 3/04/18																
242	Painting	2 days	Fri 15/06/18	Mon 18/06/18	Wed 21/03/18	Fri 23/03/18																
243	Greening	2 days	Mon 18/06/18	Tue 19/06/18	Thu 22/03/18	Thu 29/03/18																
244	Long Life	2 days	Mon 18/06/18	Tue 19/06/18	Tue 27/03/18	Tue 3/04/18																
245	Stage 4 - Queen St	207 days	Wed 12/07/17	Fri 18/05/18	Tue 18/07/17	Fri 5/01/18																
246	Stage 4A - Parking Bays CH3900-CH4100	100 days	Wed 12/07/17	Wed 29/11/17	Tue 18/07/17	Thu 10/08/17																
256	Stage 4B - Westside Copenhagen FP CH3780-CH3520	21 days	Wed 2/08/17	Thu 31/08/17	Thu 10/08/17	Wed 20/09/17																
267	Stage 4C - Eastside Copenhagen FP CH3520-CH3800	31 days	Tue 10/10/17	Wed 22/11/17	Wed 20/09/17	Wed 4/10/17																
280	Stage 4D - Retaining Wall @ Rodney	142 days	Mon 24/07/17	Fri 23/02/18	Wed 4/10/17	Fri 5/01/18																
281	Set Up TMP	0 days	Mon 24/07/17	Mon 24/07/17	NA	NA																
282	Excavate to Waste	3 days	Mon 24/07/17	Wed 26/07/17	Wed 4/10/17	Mon 9/10/17																
283	Set Up TMP	0 days	Mon 27/11/17	Mon 27/11/17	NA	NA																
284	Construct Retaining Wall	30 days	Mon 27/11/17	Fri 19/01/18	NA	NA																
285	Install Subsoil	2 days	Mon 12/02/18	Tue 13/02/18	NA	NA																
286	Kerbing Works	2 days	Wed 14/02/18	Thu 15/02/18	NA	NA																
287	Prep Footpath (Inc. Driveways)	3 days	Fri 16/02/18	Tue 20/02/18	NA	NA																
288	Pour Footpath (Inc. Driveways)	2 days	Wed 21/02/18	Thu 22/02/18	NA	NA																
289	Asphalt footpath	1 day	Fri 23/02/18	Fri 23/02/18	NA	NA																
290	Stage 4E - Rodney Intersection Area	110 days	Mon 16/10/17	Fri 6/04/18	Wed 4/10/17	Fri 5/01/18																
291	Set Up TMP	0 days	Mon 16/10/17	Mon 16/10/17	NA	NA																
292	Stage 1 - Café Side	16 days	Mon 16/10/17	Tue 7/11/17	NA	NA																
310	Stage 2 - Kindi side	9 days	Tue 7/11/17	Fri 17/11/17	NA	NA																
322	Stage 3 - Remaining Intersection Works	7 days	Tue 27/03/18	Fri 6/04/18	NA	NA																
323	Install Flashing studs and loops	1 day	Tue 27/03/18	Tue 27/03/18	Tue 10/10/17	Fri 13/10/17																

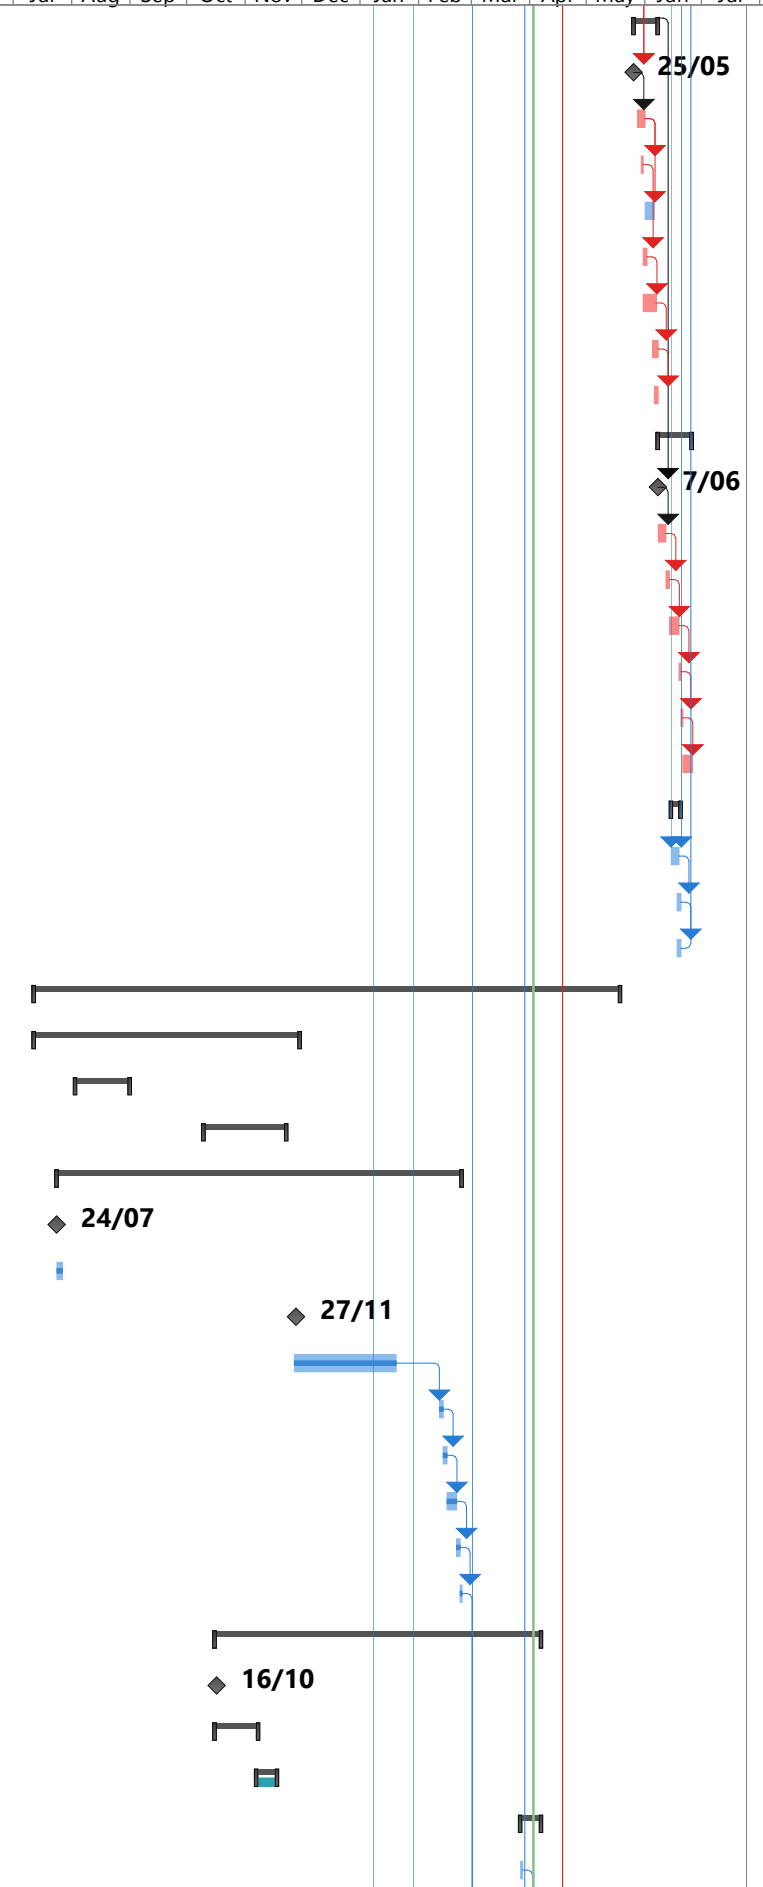

ID	Task Name	Duration	Start	Finish	Baseline Start	Baseline Finish	2017		Qtr 3, 2017			Qtr 4, 2017			Qtr 1, 2018			Qtr 2, 2018			Qtr 3, 2018	
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
324	Remove Stafford Road Traffic Islands	1 day	Tue 27/03/18	Tue 27/03/18	NA	NA																
325	Install new Stafford Road Pram Crossings and Traffic Islands	6 days	Wed 28/03/18	Fri 6/04/18	NA	NA																
326	Remove Traffic Control	0 days	Fri 6/04/18	Fri 6/04/18	NA	NA																
327	Stage 4F - Minor Works	17 days	Mon 21/08/17	Tue 12/09/17	NA	NA																
334	Stage 4 - Line-marking & Signage	38 days	Fri 23/03/18	Fri 18/05/18	Wed 1/11/17	Tue 14/11/17																
335	Painting	2 days	Wed 28/03/18	Thu 29/03/18	Wed 1/11/17	Fri 3/11/17																
336	Greening	4 days	Tue 15/05/18	Fri 18/05/18	Thu 2/11/17	Thu 9/11/17																
337	Long Life	4 days	Wed 9/05/18	Mon 14/05/18	Tue 7/11/17	Tue 14/11/17																
338	Signage	3 days	Fri 23/03/18	Tue 27/03/18	Thu 2/11/17	Thu 9/11/17																
339	Stage 4 - Snag Items	9 days	Fri 23/03/18	Fri 6/04/18	NA	NA																
340	Snagging and finishing items	9 days	Fri 23/03/18	Fri 6/04/18	NA	NA																
341	VO 1 & 5 - Watermains Relocations	97 days	Wed 12/07/17	Fri 24/11/17	NA	NA																
372	VO-2: Vincent Subsoil Crossing	3 days	Mon 31/07/17	Wed 2/08/17	NA	NA																
378	VO 14 - Eastside Copenhagen FP CH-CH	20 days	Fri 23/02/18	Fri 23/03/18	NA	NA																
379	Set Up TMP	0 days	Fri 23/02/18	Fri 23/02/18	NA	NA																
380	Environmental Controls	1 day	Mon 26/02/18	Mon 26/02/18	NA	NA																
381	Excavate to Waste	2 days	Mon 26/02/18	Tue 27/02/18	NA	NA																
382	Subsoil Installation	3 days	Wed 28/02/18	Fri 2/03/18	NA	NA																
383	Excavate and Remove Sewer Vent Pipe	2 days	Mon 5/03/18	Tue 6/03/18	NA	NA																
384	House Connections	2 days	Mon 5/03/18	Tue 6/03/18	NA	NA																
385	Utilities Relocations	4 days	Wed 7/03/18	Mon 12/03/18	NA	NA																
386	Kerbing Works	3 days	Tue 13/03/18	Thu 15/03/18	NA	NA																
387	Prep Footpath (Inc. Driveways)	4 days	Fri 16/03/18	Wed 21/03/18	NA	NA																
388	Pour Footpath (Inc. Driveways)	3 days	Wed 21/03/18	Fri 23/03/18	NA	NA																
389	Asphalt Copenhagen Path	2 days	Wed 21/03/18	Thu 22/03/18	NA	NA																
390	VO 15 - Queen Streen Road Improvements	4 days	Thu 22/03/18	Tue 27/03/18	NA	NA																
391	Mill Road	1 day	Thu 22/03/18	Thu 22/03/18	NA	NA																
392	Base Course Prep	1 day	Fri 23/03/18	Fri 23/03/18	NA	NA																
393	Chipseal	1 day	Mon 26/03/18	Mon 26/03/18	NA	NA																
394	Asphalt Lane	1 day	Tue 27/03/18	Tue 27/03/18	NA	NA																
395	NTT03 - Retaining Wall	65 days	Mon 8/01/18	Thu 12/04/18	NA	NA																
396	Retaining Wall 6	12 days	Mon 8/01/18	Tue 23/01/18	NA	NA																
397	Retaining Wall 7	53 days	Wed 24/01/18	Thu 12/04/18	NA	NA																
398	VO TBC - RW 3 watermain relocation	12 days	Mon 26/03/18	Thu 12/04/18	NA	NA																
399	Lay pipe	1 day	Mon 26/03/18	Mon 26/03/18	NA	NA																
400	Watercare - notification	10 days	Tue 27/03/18	Wed 11/04/18	NA	NA																
401	Watercare - connection	1 day	Thu 12/04/18	Thu 12/04/18	NA	NA																

